

	(A)	Nome	Durata	Data di Avvio	Data di chiusura	Predecessori
1		Activity Start	0 giorni	28/03/22 8.00	28/03/22 8.00	
2		First meeting with the team	1 giorno	28/03/22 8.00	28/03/22 17.00	
3		Work definition	1 giorno	28/03/22 8.00	28/03/22 17.00	1
4		Role definition and assignment	1 giorno	28/03/22 8.00	28/03/22 17.00	1
5		Requirement document	7 giorni	29/03/22 8.00	06/04/22 17.00	
6		Definition of Stakeholders	1 giorno	29/03/22 8.00	29/03/22 17.00	3;4
7		Definition of Context diagram and interfaces	1 giorno	29/03/22 8.00	29/03/22 17.00	3;4
8		Description of Stories and Personas	1 giorno	30/03/22 8.00	30/03/22 17.00	3FS+1 giorno;4
9		Definition of FRs and NFRs	3 giorni	30/03/22 8.00	01/04/22 17.00	3FS+1 giorno;4
10		Use Case Diagram Design	1 giorno	04/04/22 8.00	04/04/22 17.00	9
11		Definition of Use Cases and Scenarios	1 giorno	05/04/22 8.00	05/04/22 17.00	10
12		Definition of Glossary	1 giorno	06/04/22 8.00	06/04/22 17.00	11
13		System Design	1 giorno	06/04/22 8.00	06/04/22 17.00	12SS
14		Deployment Diagram Design	1 giorno	06/04/22 8.00	06/04/22 17.00	12SS
15		Requirement Document Completion	0 giorni	06/04/22 17.00	06/04/22 17.00	6;7;8;14
16		GUI Prototype	4 giorni	07/04/22 8.00	12/04/22 17.00	
17		GUI design	4 giorni	07/04/22 8.00	12/04/22 17.00	15
18		GUI Prototype Completion	0 giorni	12/04/22 17.00	12/04/22 17.00	17
19		Design Document	10 giorni	13/04/22 8.00	26/04/22 17.00	
20		Design high level architecture	5 giorni	13/04/22 8.00	19/04/22 17.00	15;18
21		Detail design	5 giorni	20/04/22 8.00	26/04/22 17.00	20
22		Design Document Completion	0 giorni	26/04/22 17.00	26/04/22 17.00	21
23		Code Development	20 giorni	27/04/22 8.00	24/05/22 17.00	
24		Project Creation	1 giorno	27/04/22 8.00	27/04/22 17.00	15;18;22
25		Classes Creation	2 giorni	28/04/22 8.00	29/04/22 17.00	24
26		Database Creation	2 giorni	02/05/22 8.00	03/05/22 17.00	25
27		Frontend Development	7 giorni	04/05/22 8.00	12/05/22 17.00	26
28		Backend Development	10 giorni	11/05/22 8.00	24/05/22 17.00	27SS+5 giorni
29		Code Completion	0 giorni	24/05/22 17.00	24/05/22 17.00	28
30		Unit Test	4 giorni	25/05/22 8.00	30/05/22 17.00	
31		Requirements tests	4 giorni	25/05/22 8.00	30/05/22 17.00	29
32		Unit test completion	0 giorni	30/05/22 17.00	30/05/22 17.00	31
33		API Test	4 giorni	31/05/22 8.00	03/06/22 17.00	
34		User interaction Tests	2 giorni	31/05/22 8.00	01/06/22 17.00	32
35		Load Test	1 giorno	02/06/22 8.00	02/06/22 17.00	34



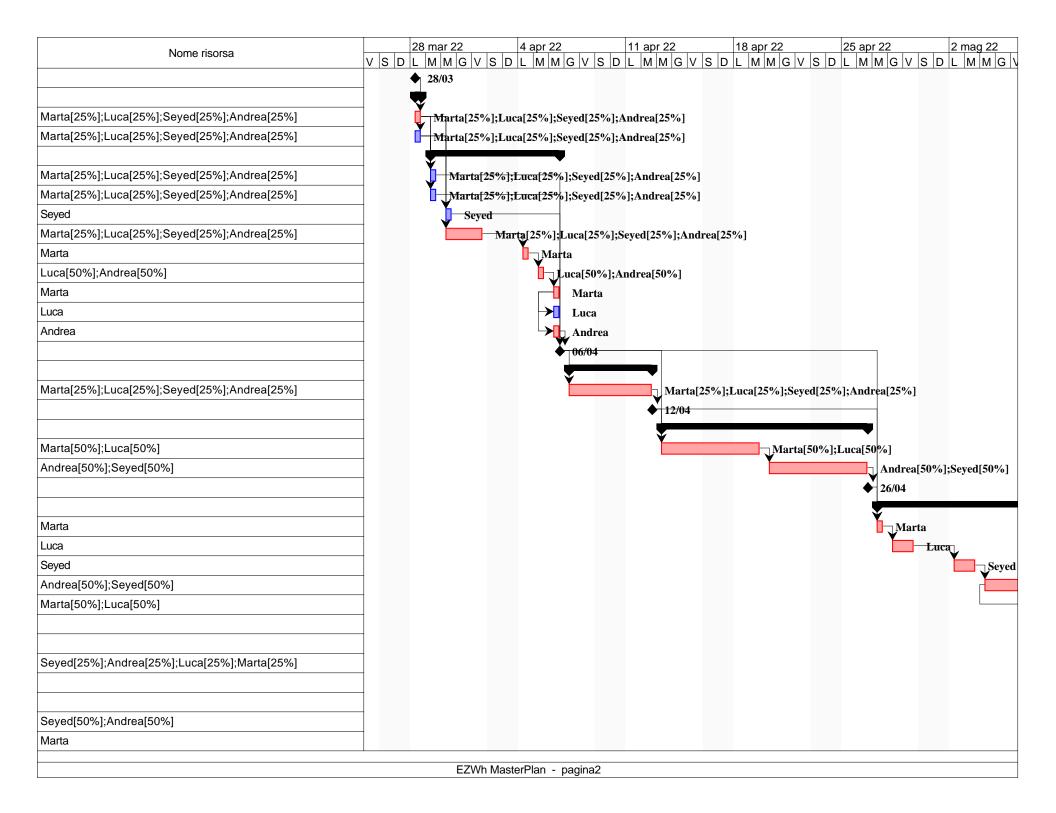

	(B)	Nome	Durata	Data di Avvio	Data di chiusura	Predecessori
36		Security Test	1 giorno	03/06/22 8.00	03/06/22 17.00	35
37		API Test Completion	0 giorni	03/06/22 17.00	03/06/22 17.00	36
38		Management Documents	4 giorni	06/06/22 8.00	09/06/22 17.00	
39		Management Documents Preparation	4 giorni	06/06/22 8.00	09/06/22 17.00	37
40		Management Documents Delivery	0 giorni	09/06/22 17.00	09/06/22 17.00	39

		_		T		T		T		T	
Nome risorsa		28 mar 22		4 apr 22		11 apr 22		18 apr 22		25 apr 22	2 mag 22
Nome horiou	V S D	L M M G	V S D	L M M G V	S D	L M M G V	S D	L M M G V	S D	L MMGV	2 mag 22 S D L M M G
Luca											
Marta[25%];Luca[25%];Seyed[25%];Andrea[25%]											
Marta[25/6],Euca[25/6],Seyeu[25/6],Andrea[25/6]											
		EZ	\//h \//oct	erPlan - pagina	26						
		EZ	vvii iviast	errian - pagin	aυ						

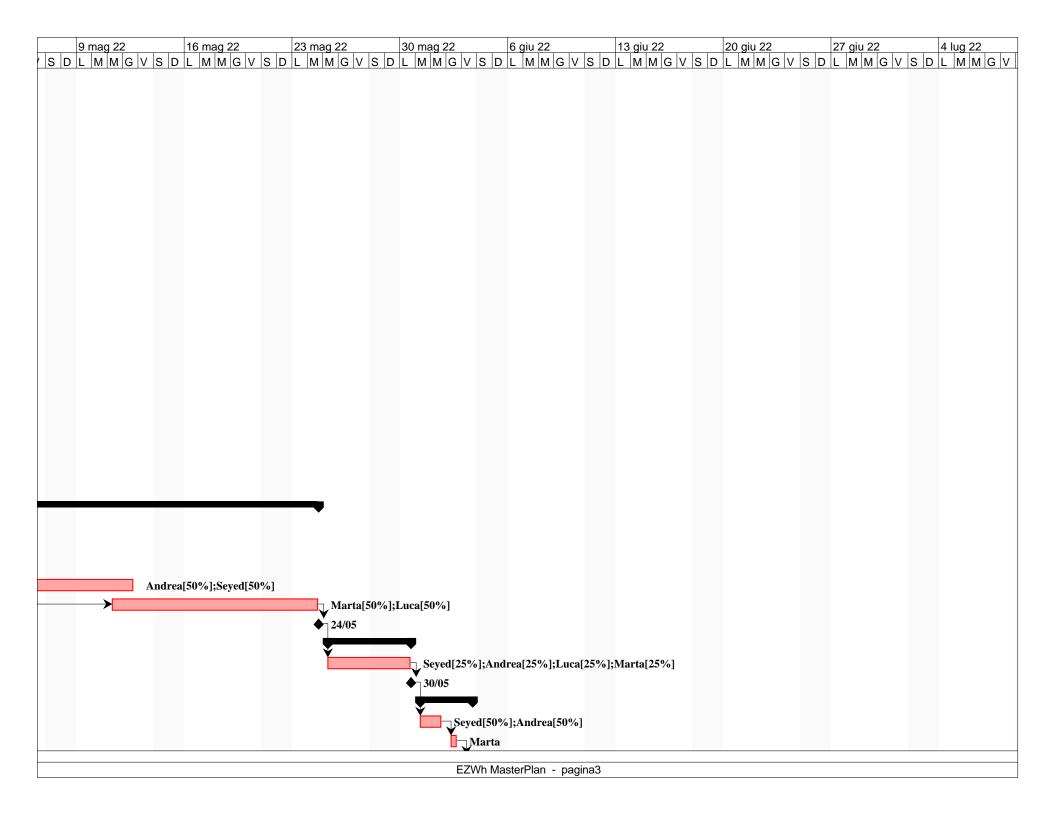
